Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	24 September 2026
Team ID	Individual
Project Name	Automated Incident Management Lifecycle using ServiceNow
Maximum Marks	4 Marks

Product Backlog, Sprint Schedule, and Estimation

The product backlog below is prepared for the ServiceNow Automated Incident Management Lifecycle project.

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Incident Creation & Classification	US-01	As a Service Desk agent, I can create an incident in Service Operations Workspace with caller and short description.	2	High	Venkata Karthik Muppidi
Sprint-1	Incident Classification	US-02	As a Service Desk agent, I can classify an incident using Category, Subcategory, Urgency, Service, Service Offering, and CI.	3	High	Venkata Karthik Muppidi
Sprint-1	Knowledge Integration	US-03	As a Service Desk agent, I can use Agent Assist to find relevant Knowledge Articles and attach a helpful article to the incident.	3	High	Venkata Karthik Muppidi
Sprint-2	Reassignment & Escalation	US-04	As a Service Desk agent, I can reassign an incident to the appropriate Level 2 support group and maintain activity updates.	3	High	Venkata Karthik Muppidi
Sprint-2	Change Management	US-05	As a support technician, I can create and link an emergency change request when incident resolution requires a change.	3	High	Venkata Karthik Muppidi
Sprint-3	Child Incident Management	US-06	As a support technician, I can create a child incident to track a recurring or related issue and link it to the parent incident.	2	High	Venkata Karthik Muppidi
Sprint-3	Incident Resolution	US-07	As a Level 2 technician, I can document probable cause, resolution code, and resolution notes and resolve the incident.	3	High	Venkata Karthik Muppidi
Sprint-4	Knowledge & SLA	US-08	As an administrator, I can create a Knowledge Article from a resolved incident and verify SLA and related-record tracking.	3	High	Venkata Karthik Muppidi
Sprint-4	Validation & Collaboration	US-09	As an administrator, I can validate parent/child resolution, change linkage, knowledge creation, SLA visibility, and multi-team activity.	2	High	Venkata Karthik Muppidi

Sprint Planning & Project Tracker

Sprint Schedule

Four planned sprints organize the project work. Actual dates can be entered during execution.

Sprint	User Stories	Story Points	Planned Scope
Sprint-1	US-01 to US-03	8	Incident creation, classification, Service/CI data, and Knowledge integration
Sprint-2	US-04 to US-05	6	Level 2 reassignment, escalation, and emergency change integration
Sprint-3	US-06 to US-07	5	Child incidents, cause documentation, and incident resolution
Sprint-4	US-08 to US-09	5	Knowledge creation, SLA/related records, and end-to-end validation

Project Tracker

Sprint	Total Story Points	Status	Sprint Start Date	Sprint End Date (Planned)	Sprint Release Date (Actual)
Sprint-1	8	Planned	TBD	TBD	TBD
Sprint-2	6	Planned	TBD	TBD	TBD
Sprint-3	5	Planned	TBD	TBD	TBD
Sprint-4	5	Planned	TBD	TBD	TBD

Velocity

Velocity represents the amount of work completed by the team during a sprint, measured in story points. This project has 24 planned story points across four sprints.


Planned average velocity = 24 story points ÷ 4 sprints = 6 story points per sprint.

Actual velocity should be calculated after each sprint using the story points actually completed. No actual completion values have been a

Burndown Chart

A burndown chart is a graphical representation of work left to do versus time. It is commonly used in Agile software development methodologies such as Scrum.

For this project, the chart tracks remaining story points as the ServiceNow Automated Incident Management Lifecycle work progresses toward completion. The project has 24 planned story points.

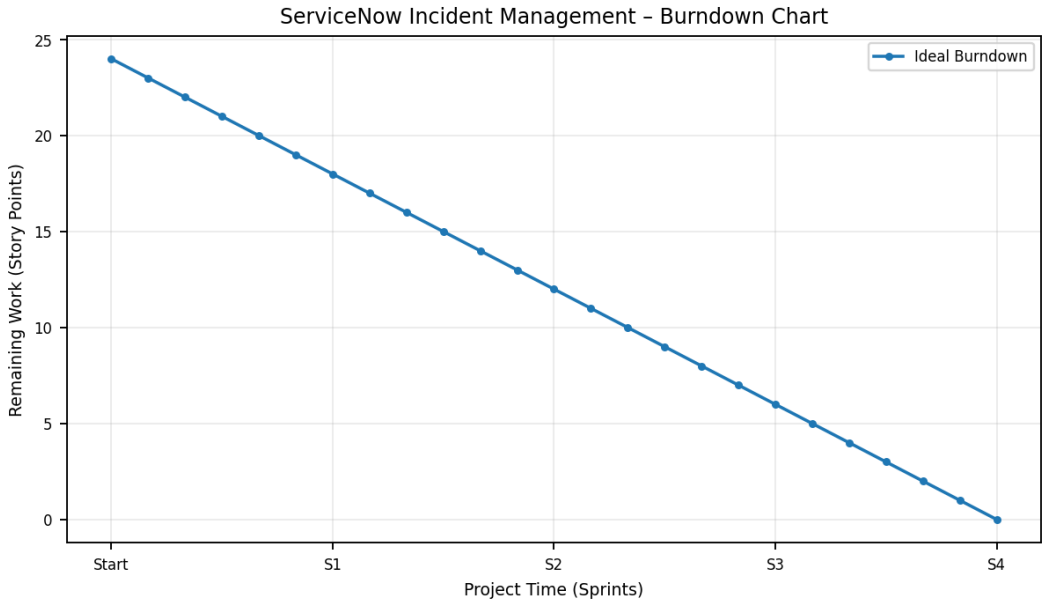

How to interpret the chart

- The X-axis represents project time in sprints.
- The Y-axis represents remaining work in story points.
- The ideal line starts at 24 story points and decreases to 0.
- The actual burndown should be updated during execution using the remaining story points.
- If actual work remains above the ideal line, the project may be behind the planned schedule.

Planned Burndown Values

Stage	Ideal Remaining Story Points	Actual Remaining Story Points
Project Start	24	TBD
End of Sprint-1	16	TBD
End of Sprint-2	11	TBD
End of Sprint-3	5	TBD
End of Sprint-4	0	TBD

Project Planning Details

Project Objective

To standardize and automate the lifecycle of IT incidents through ServiceNow Incident Management, from incident creation and classification through knowledge assistance, Level 2 escalation, emergency change integration, child incident tracking, resolution, Knowledge Article creation, and SLA visibility.

Planned Work by Project Area

Project Area	Planned Work
Incident Creation	Configure incident creation in Service Operations Workspace with caller, short description, and standard intake.
Incident Classification	Configure Category, Subcategory, Urgency, Service, Service Offering, and Configuration Item.
Knowledge / Agent Assist	Enable Agent Assist, review relevant Knowledge Articles, mark useful content, and attach an article to the incident.
Reassignment & Escalation	Route incidents to the appropriate Level 2 support group and maintain work notes and ownership.
Change Management	Create and link emergency change requests directly from incidents when a change is required for resolution.
Child Incidents	Create and relate child incidents for recurring or related issues and maintain parent-child tracking.
Resolution & Knowledge	Capture probable cause, resolution code, and resolution notes; resolve the incident and create Knowledge Articles.
SLA & Validation	Verify SLA tracking, related records, parent/child resolution, change linkage, knowledge creation, and collaboration.

Acceptance Criteria

- Service Desk agents can create incidents in Service Operations Workspace.
- Incident classification captures Category, Subcategory, Urgency, Service, Service Offering, and CI.
- Relevant Knowledge Articles appear through Agent Assist and can be attached to the incident.
- Incidents can be reassigned to Level 2 support with ownership and activity updates maintained.
- Emergency change requests can be created and linked from incidents when required.
- Child incidents can be created and verified from the parent incident's related records.
- Probable cause, resolution code, and resolution notes can be recorded and the incident can be resolved.
- A Knowledge Article can be created from a resolved incident and SLA/related records remain visible.

Project Planning Summary

Item	Project-Specific Details
Project Name	Automated Incident Management Lifecycle using ServiceNow
Team	Individual
Team Member	Venkata Karthik Muppidi
Platform	ServiceNow
Planned User Stories	9
Planned Story Points	24
Planned Sprints	4
Primary Support Team	Service Desk / Level 2 Network Support
Core ServiceNow Records	Incident, Task SLA, Change Request, Knowledge, Child Incident, User / Group records
